


7/13 (水)


前日の搬入

工区	建方部材	数量
A	1C	4
	2G	3
	2B	9
	p	4
	2FD	5
	v	2
	3G	3
	3B	9
	p	4
	3FD	5
	v	2
	計	50
荷受	階段間柱	1
	鉄骨階段	5

柱最遠最大部材 2.0t

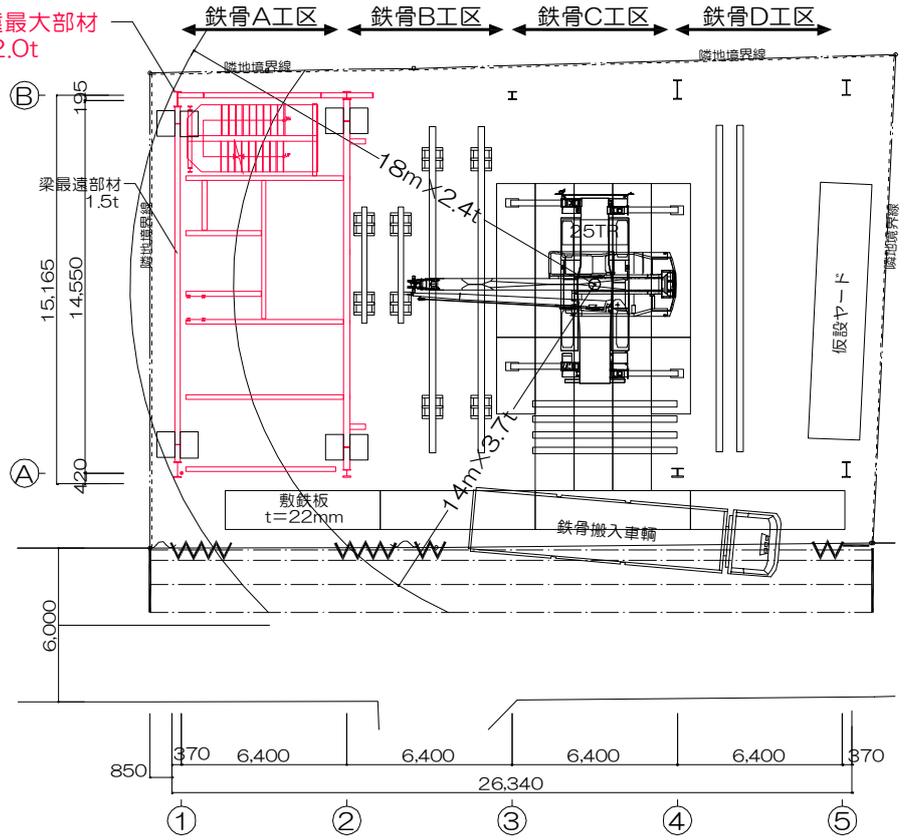



※ 建て入れ調整まで完了させる

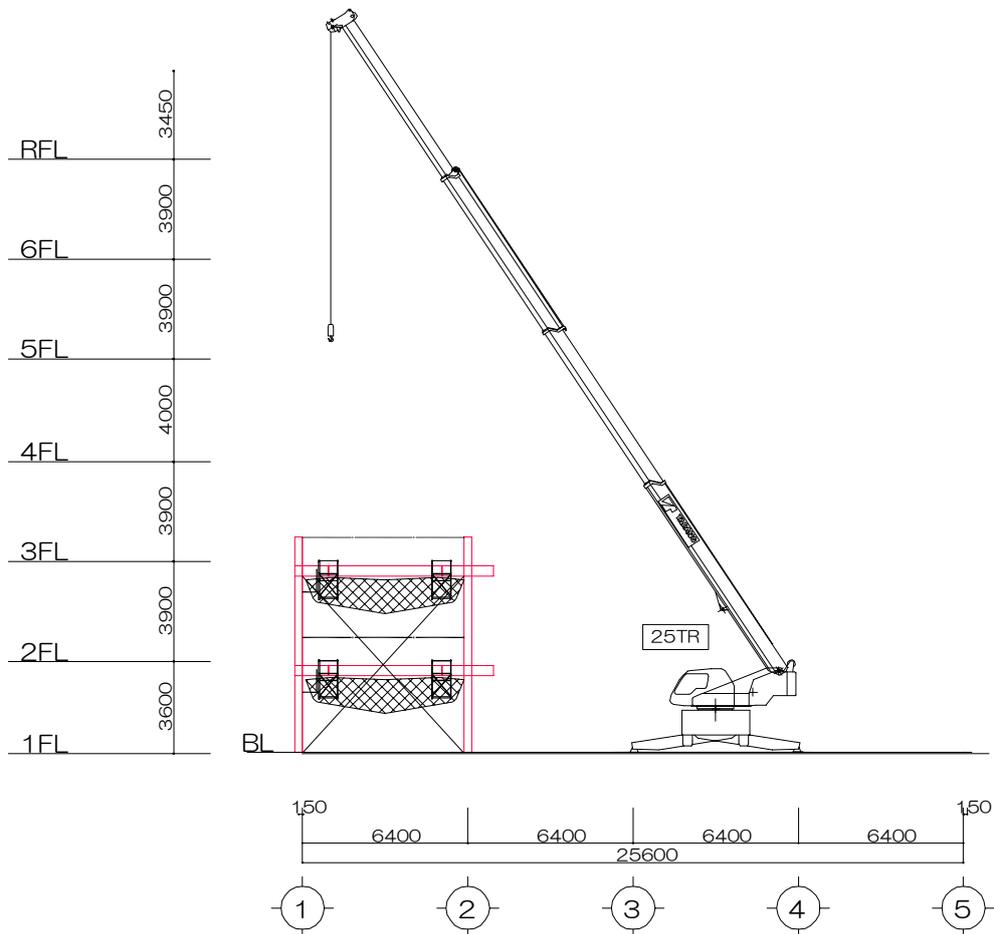

1日目

7/14 (木)



工区	建方部材	数量
A	階段間柱	1
	鉄骨階段	5
	2C	4
	4G	3
	4B	9
	p	4
	4FD	5
	v	2
	5G	4
	計	38
荷受	5B	8
	p	4

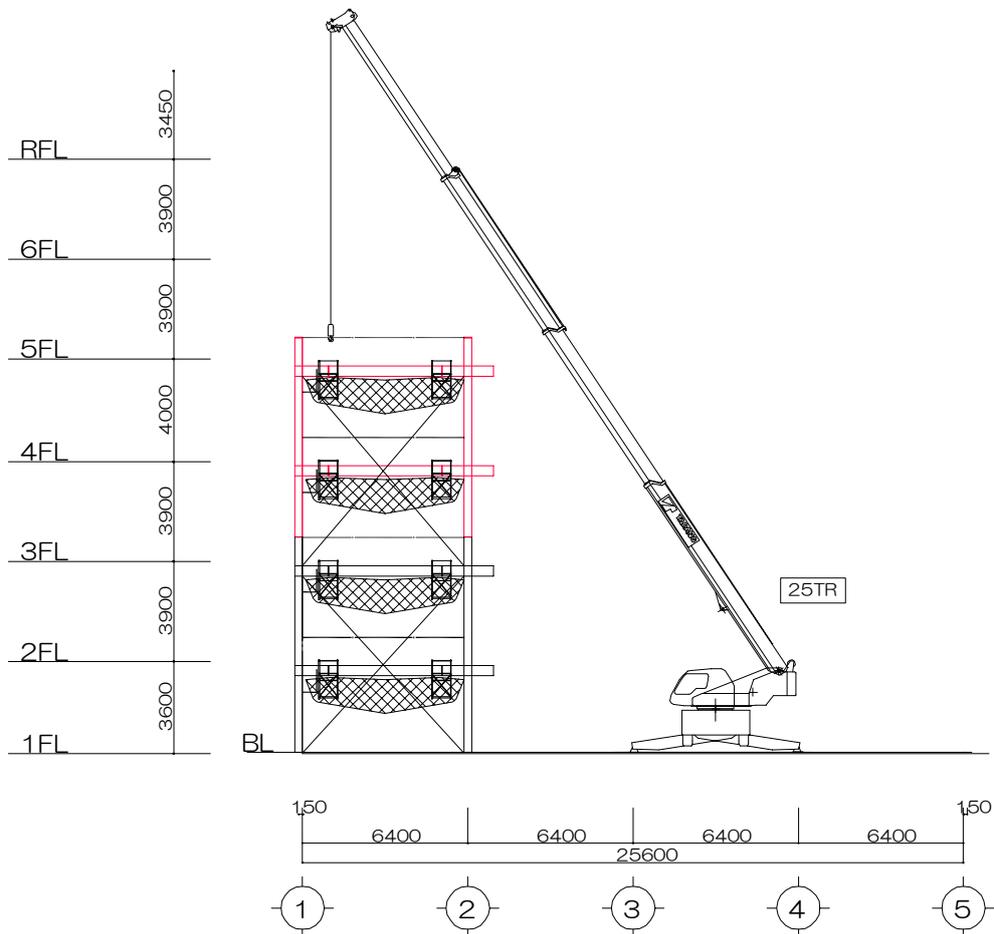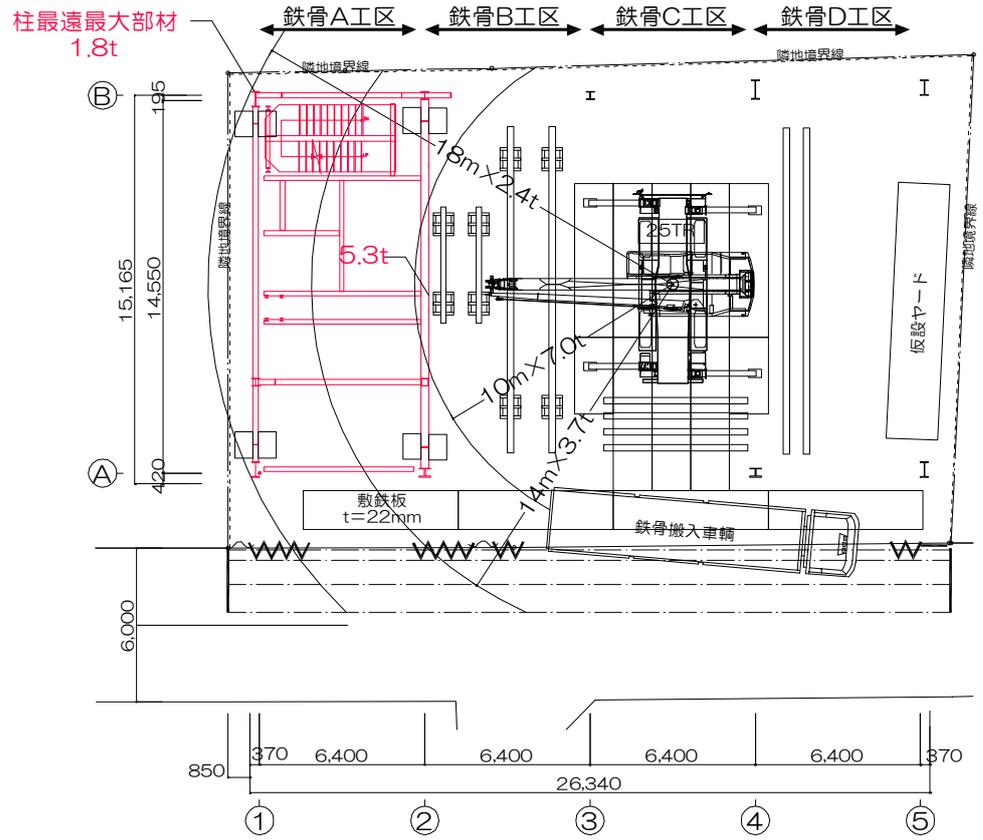

2日目

7/15 (金)





工区	建方部材	数量
A	5B	8
	p	4
	v	2
	階段間柱	1
	鉄骨階段	4
	3C	2
	c	2
	6G	5
	6B	6
	6FD	4
	計	38
荷受		
	c	2

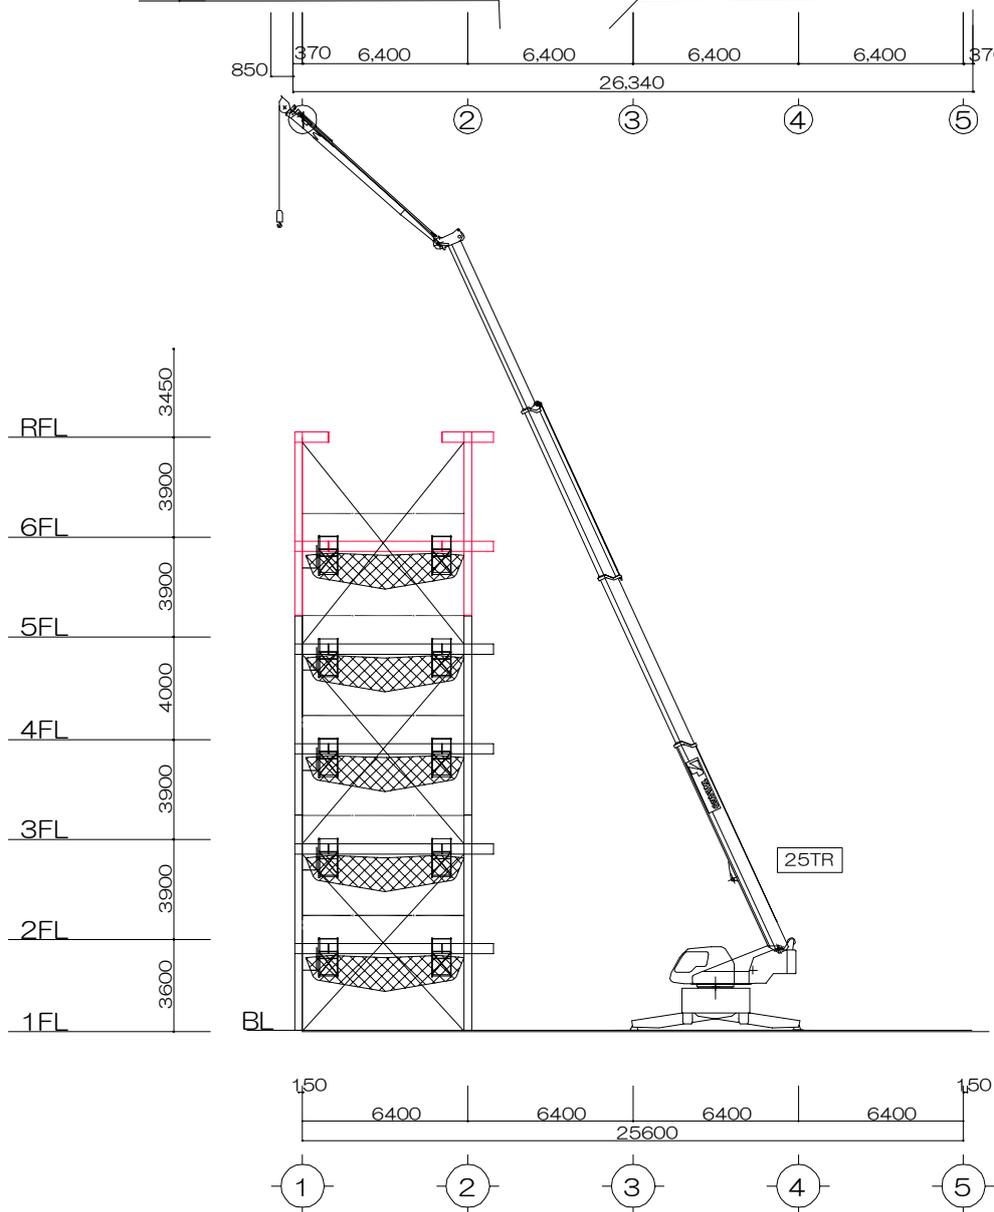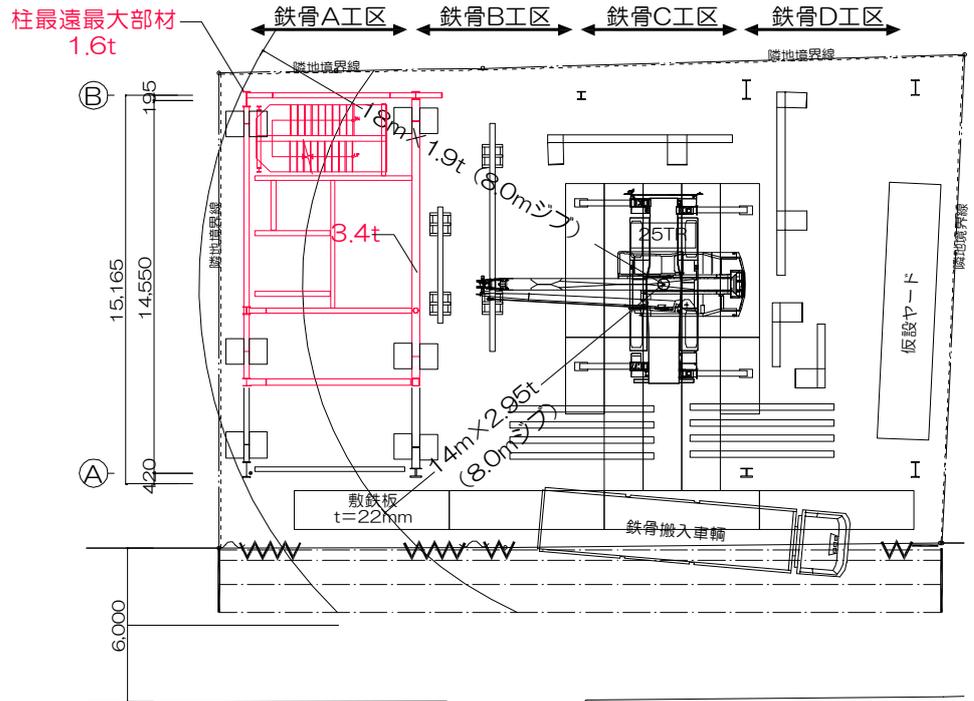

3日目

7/16 (土)



工区	建方部材	数量
A	c	2
	RG	4
	RB	7
	RFD	2
	階段間柱	1
	鉄骨階段	4
	目隠柱	5
	目隠梁	8
	設備柱	1
	設備梁	9
	計	43
荷受	1C	2

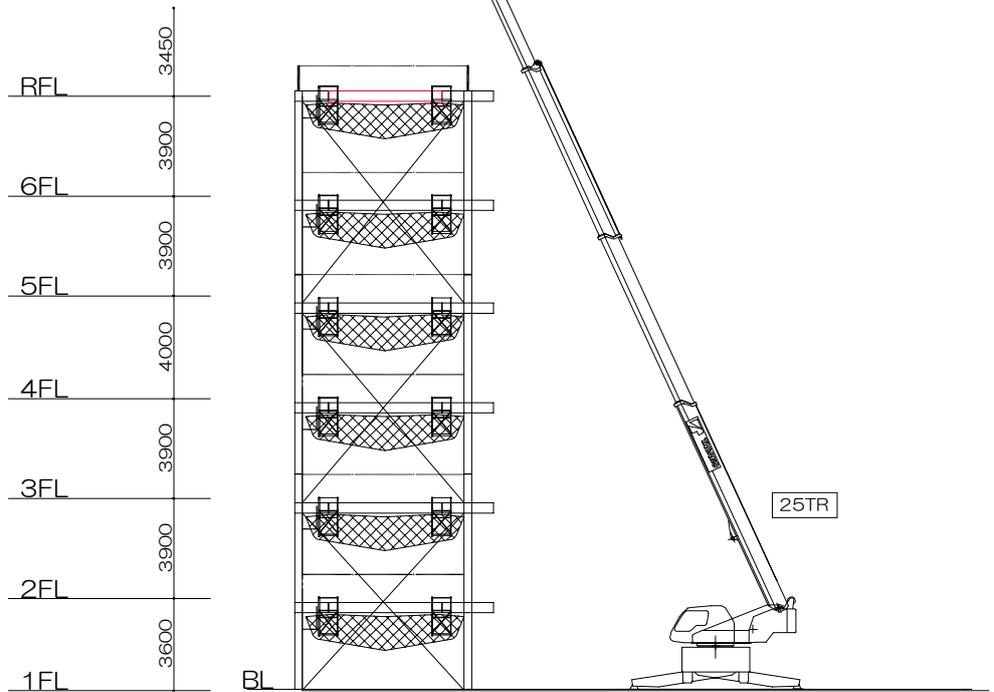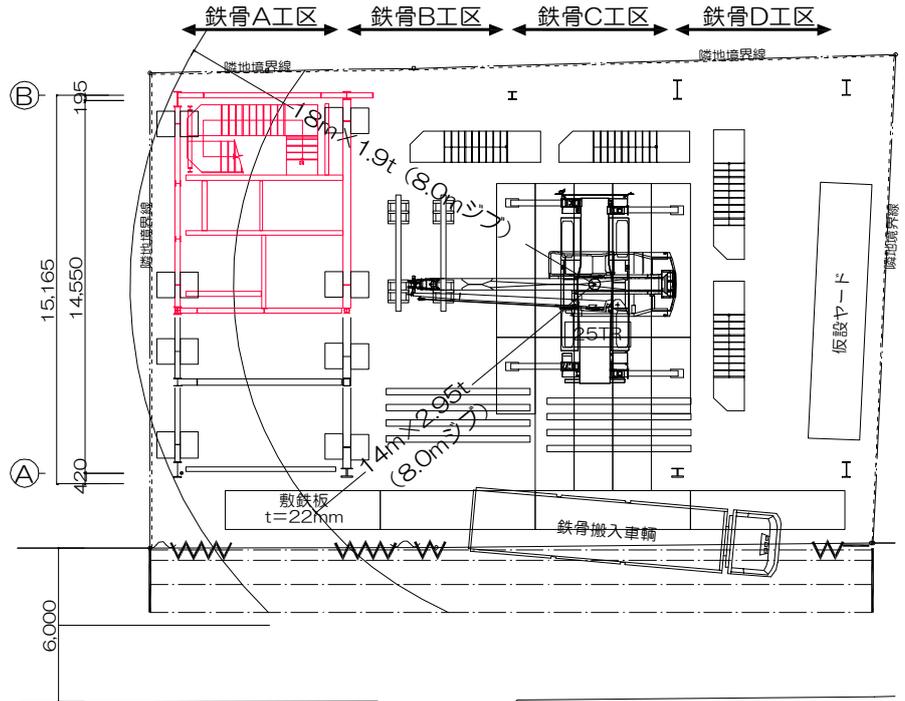

4日目

7/18 (月)



工区	建方部材	数量
B	1C	2
	2G	2
	2B	6
	v	2
	2F鉄筋	11
	2FH7B	1
	2F足場	3
	3G	2
	3B	6
	v	2
	スタッド	1
	計	38
荷受	3F鉄筋	5

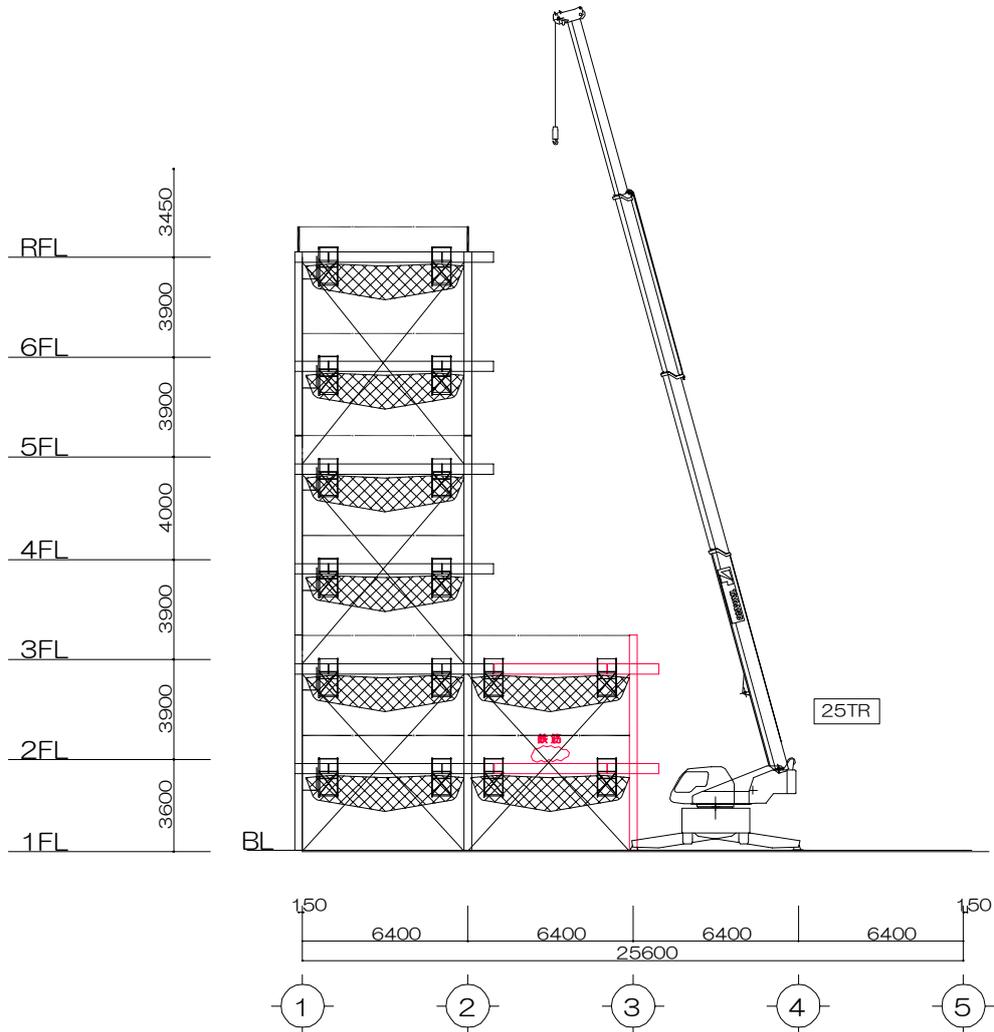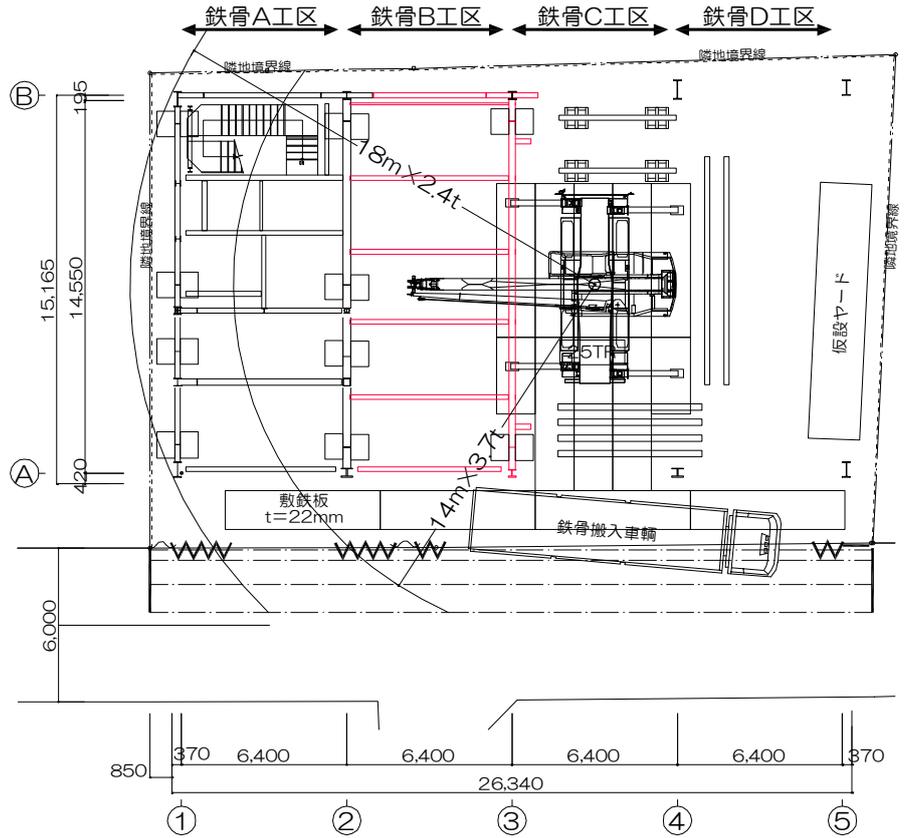

5日目

7/19 (火)



工区	建方部材	数量
B	3F鉄筋	5
	3F鉄筋	10
	3FH7B	1
	3F足場	5
	2C	2
	4G	2
	4B	6
	v	2
	4F鉄筋	10
	計	43
荷受	4F鉄筋	7

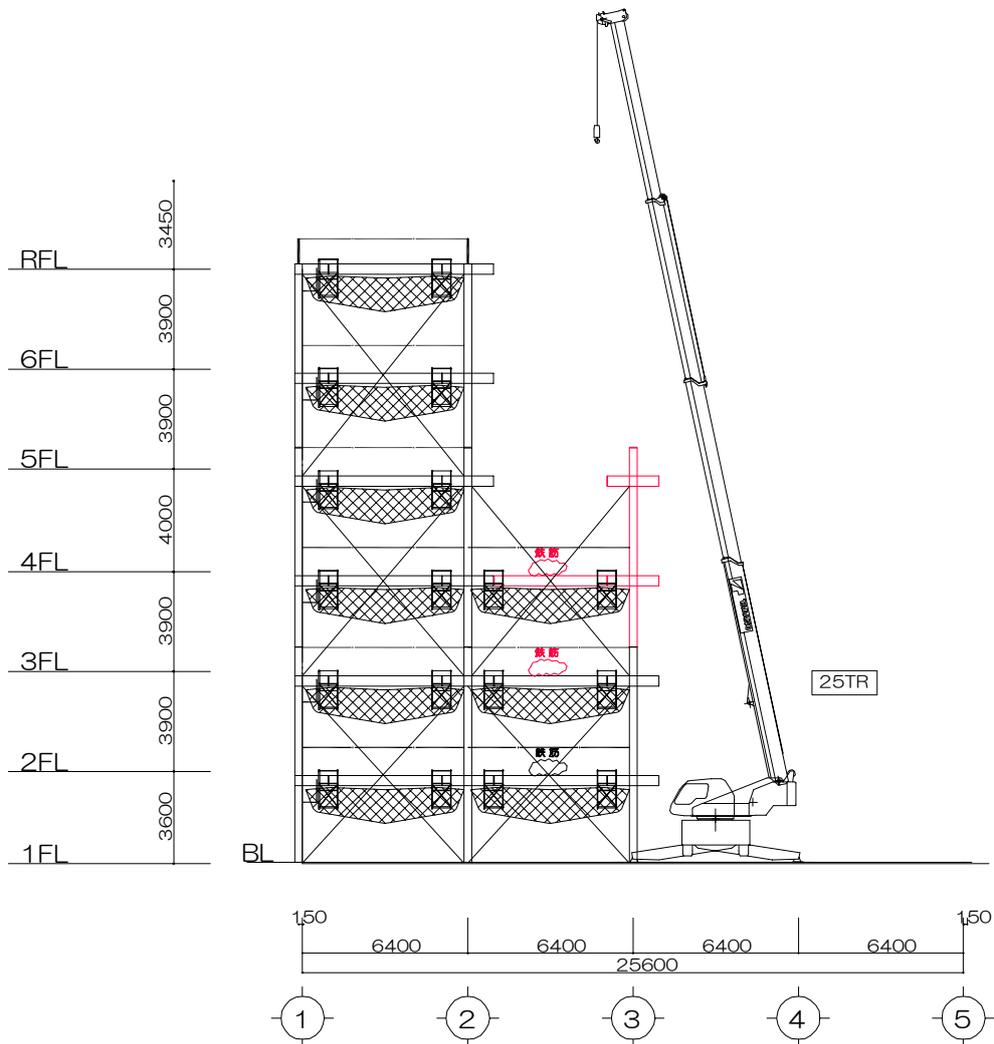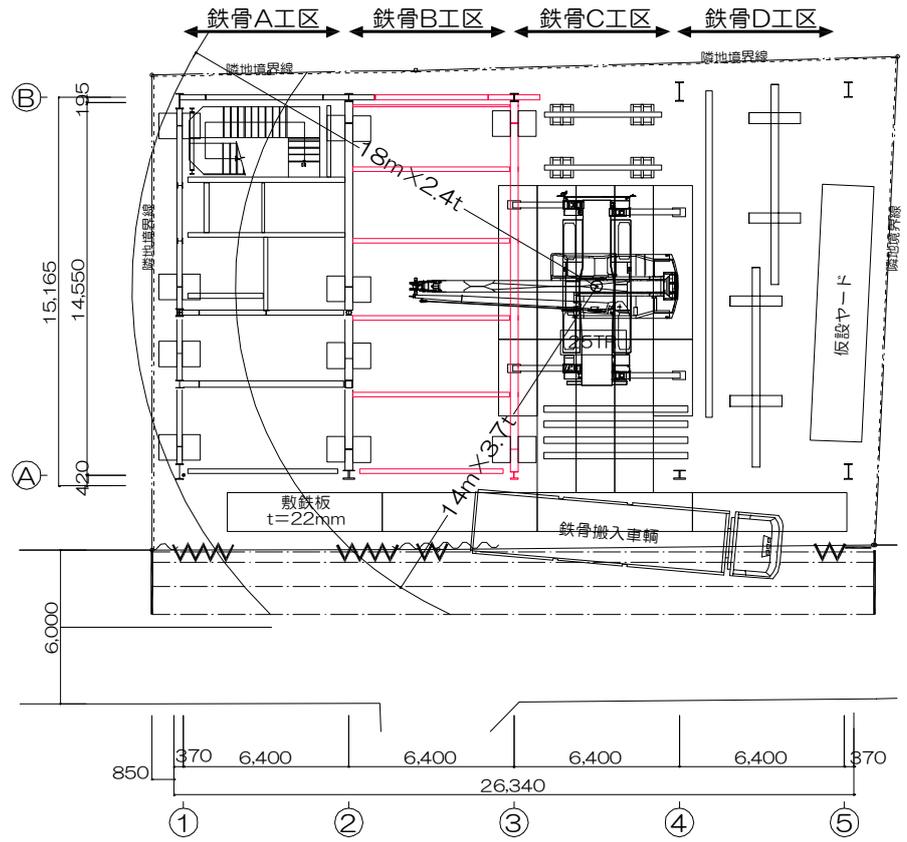

6日目

7/20 (水)



工区	建方部材	数量
B	4F鉄筋	7
	4FHFB	1
	4F足場	3
	5G	3
	5B	5
	v	2
	5F鉄筋	11
	5FHFB	1
	スタッド	1
	3C	1
	c	1
	6G	4
	計	40
荷受		
	6B	4

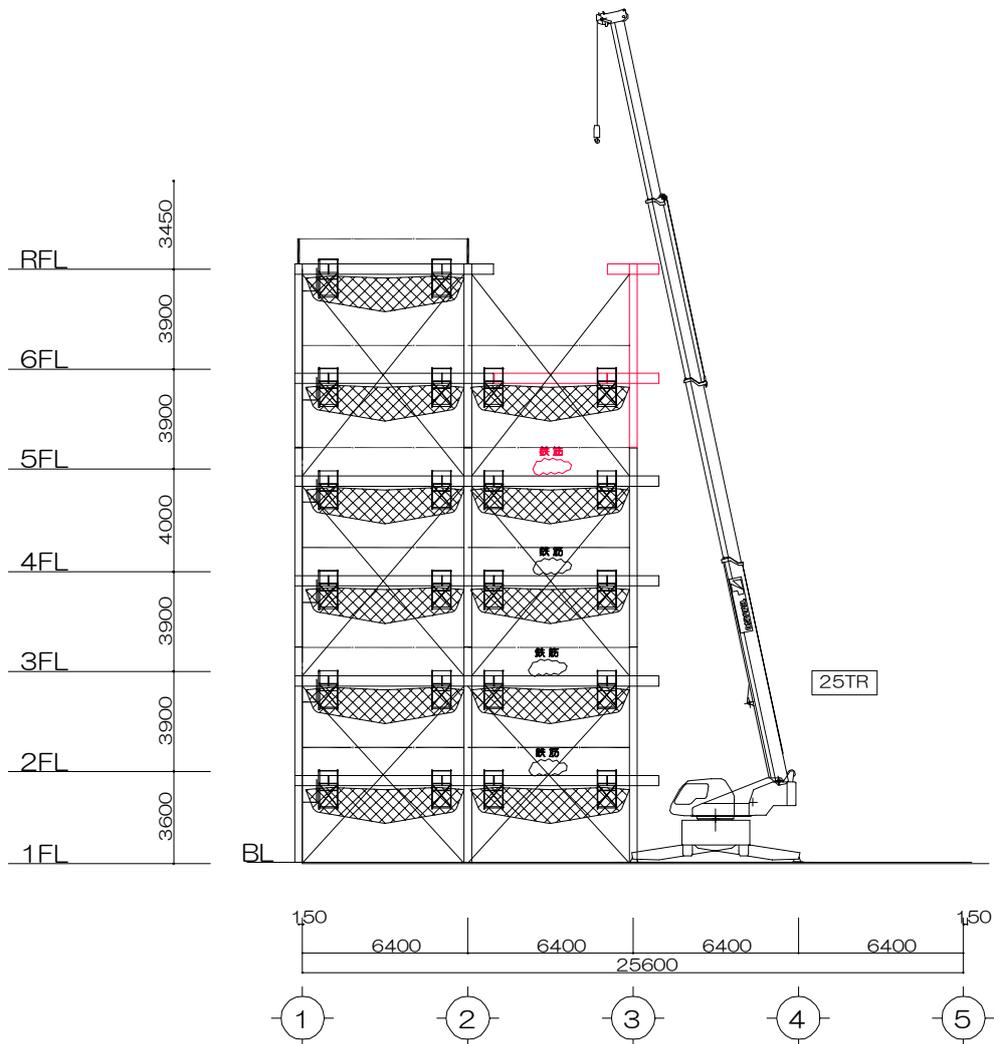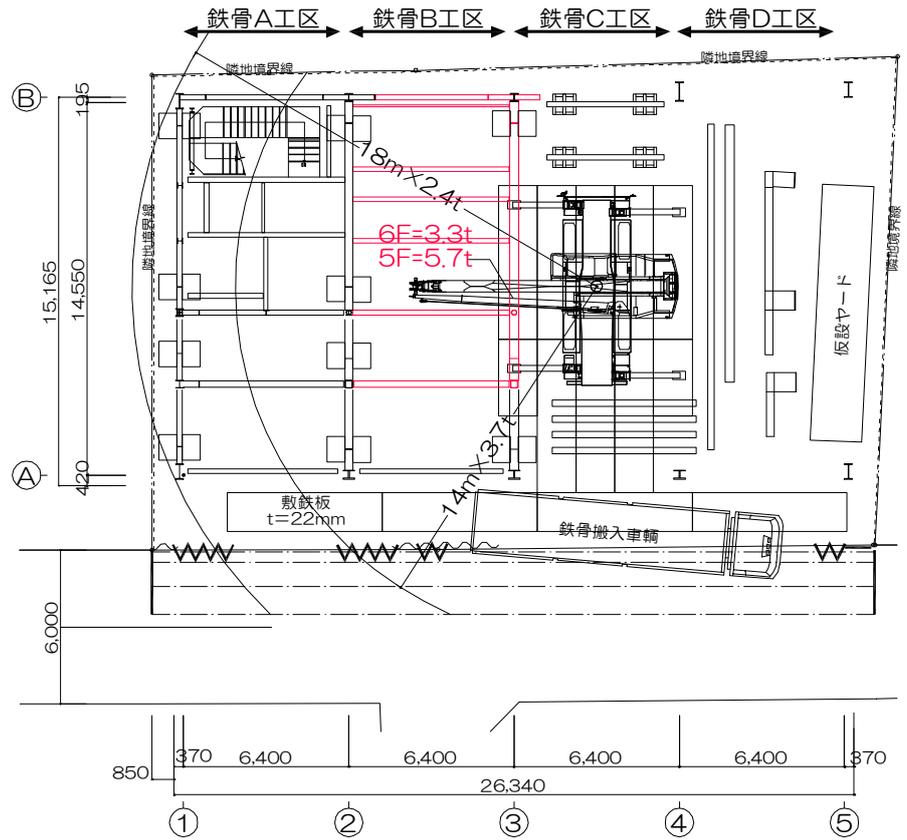

7日目

7/21 (木)



工区	建方部材	数量
B	5F足場	5
	6B	4
	6F鉄筋	11
	6FHTB	1
	c	1
	RG	3
	RB	3
	RF鉄筋	8
	RFHTB	1
	スタッド	1
	目隠柱	2
	目隠梁	4
	計	44
荷受	設備柱	1
	設備梁	6

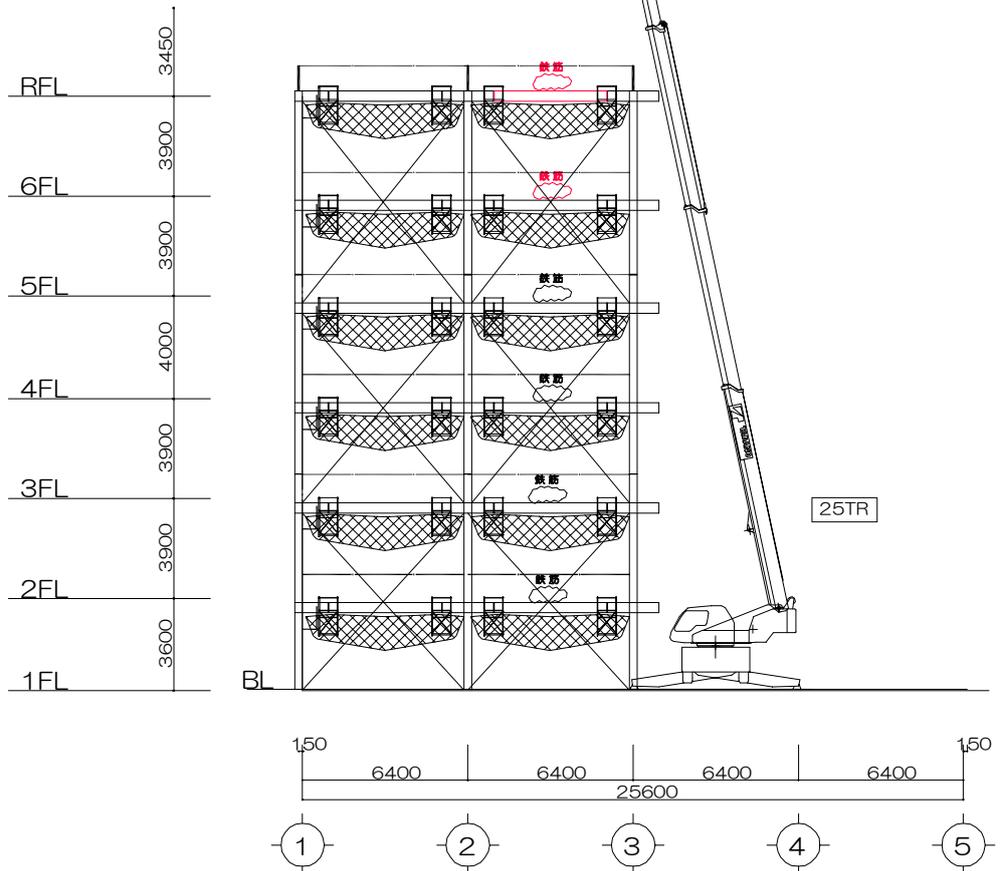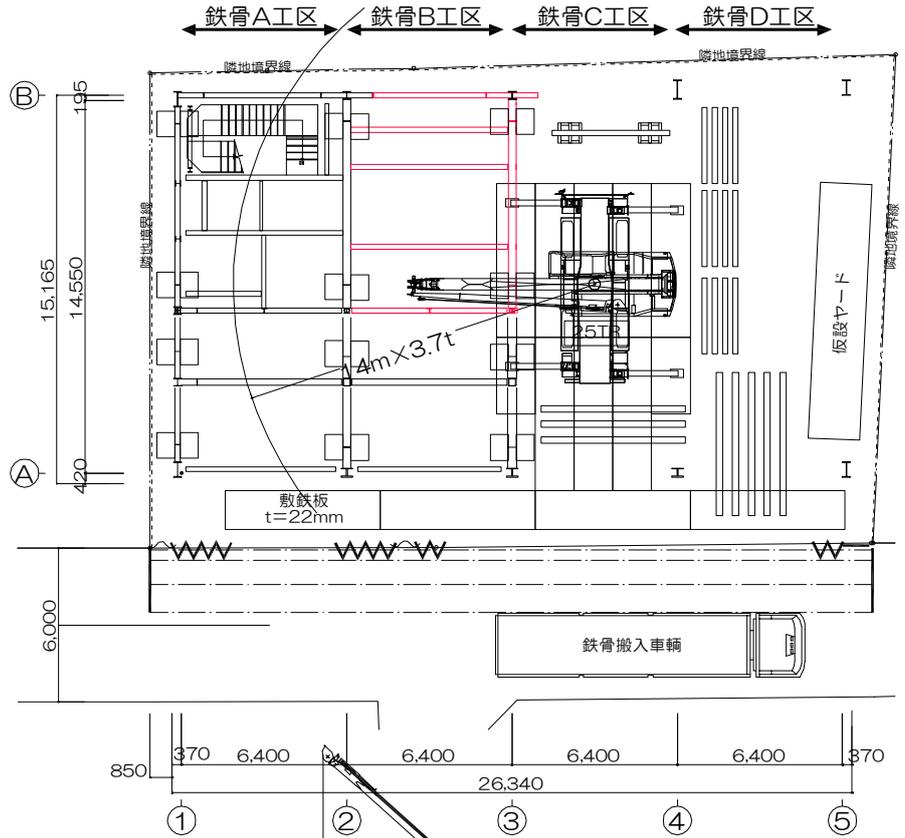

8日目

7/22 (金)

工区	建方部材	数量
B	6.RF足場	3
	設備柱	1
	設備梁	6
D	1C	4
	2G	4
	2B	6
	v	2
	2FD	4
	2F鉄筋	4
	計	34
荷受	HTB	6
	3G	4

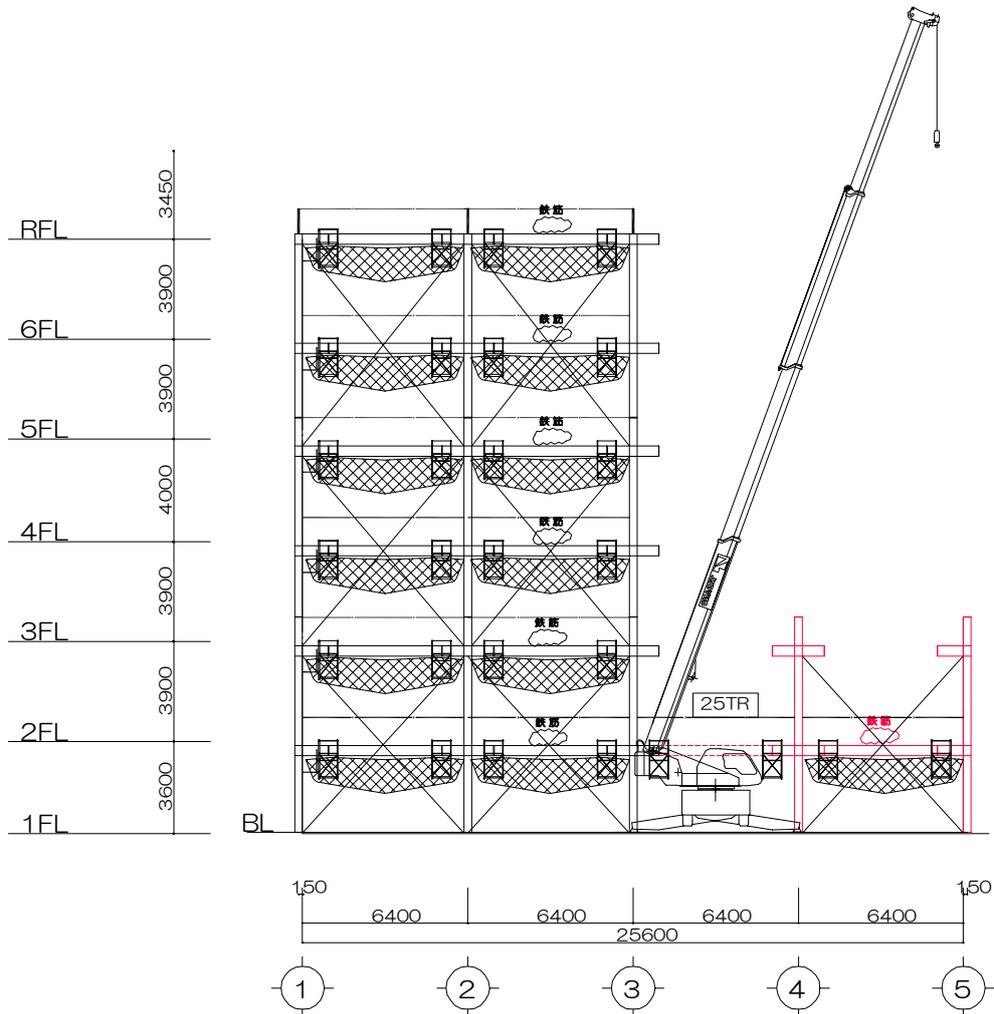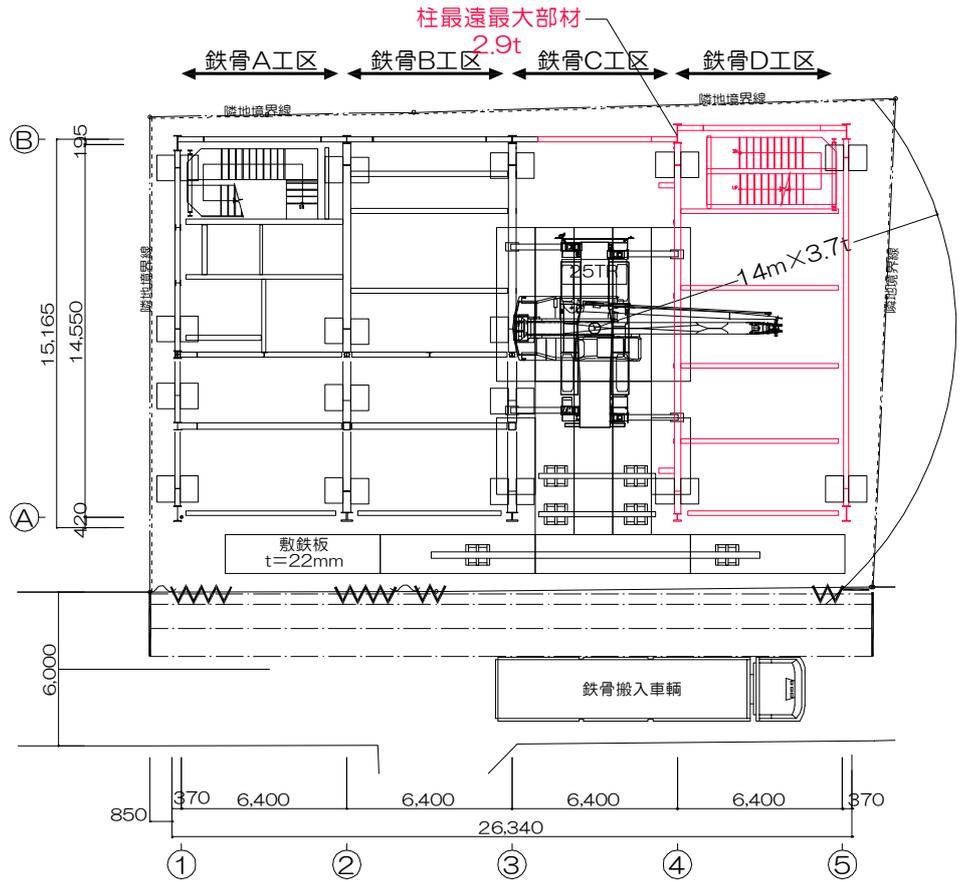



9日目

7/23 (土)

※祭り

工区	建方部材	数量
D	2F足場	3
	2FH7B	1
	3G	4
	3B	6
	3FD	2
	v	2
	3F鉄筋	10
	計	28



荷受は11:30まで完了させる

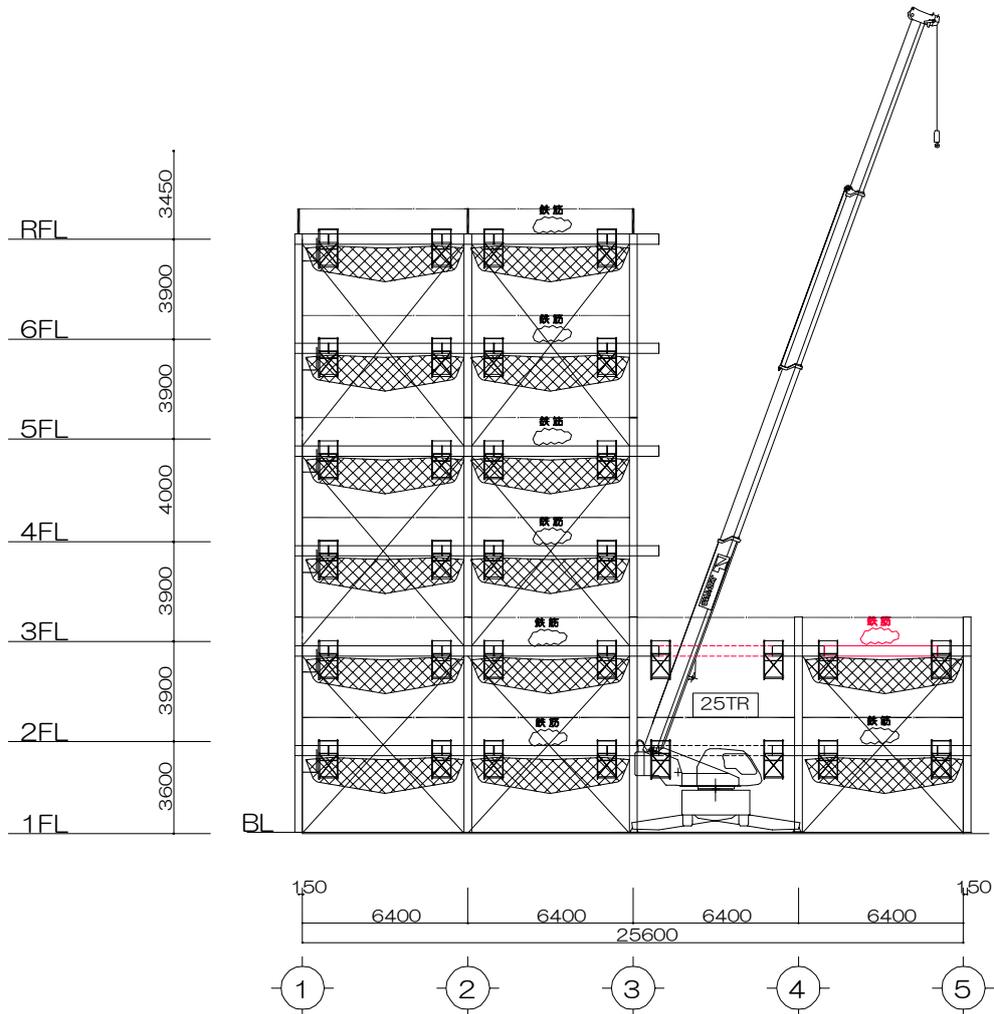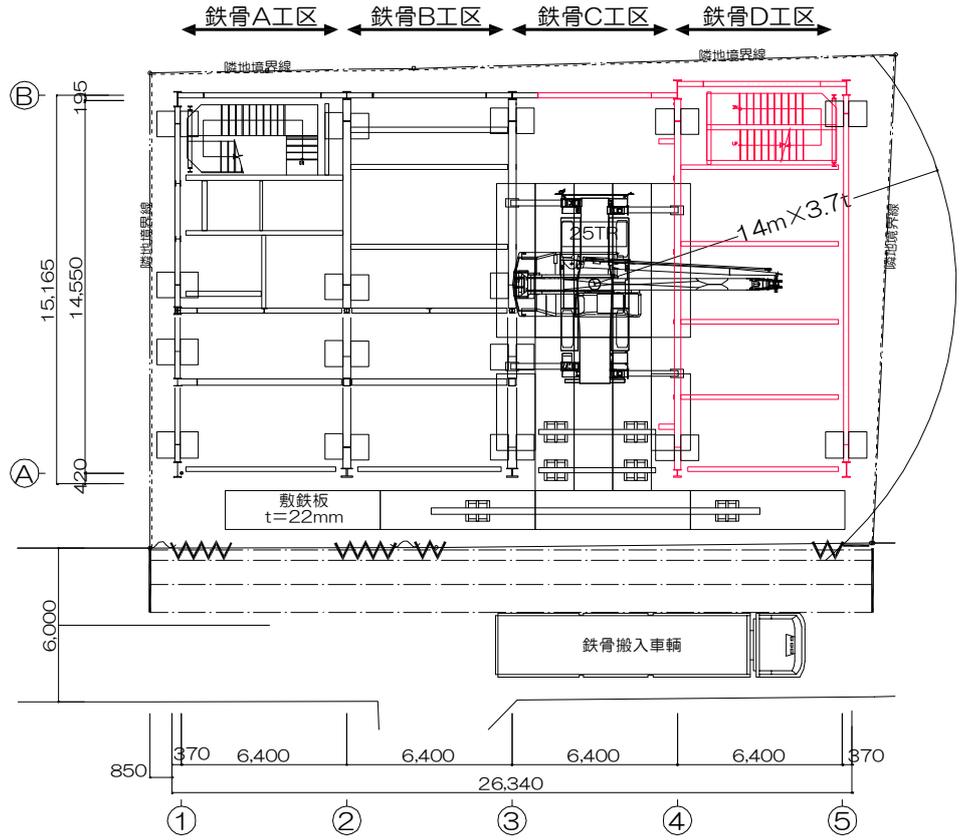

10日目

7/25 (月)



工区	建方部材	数量
D	3F足場	5
	3FHFB	1
	階段間柱	4
	鉄骨階段	4
	2C	4
	4G	4
	4B	7
	4FD	4
	4FHFB	1
	v	2
	計	34

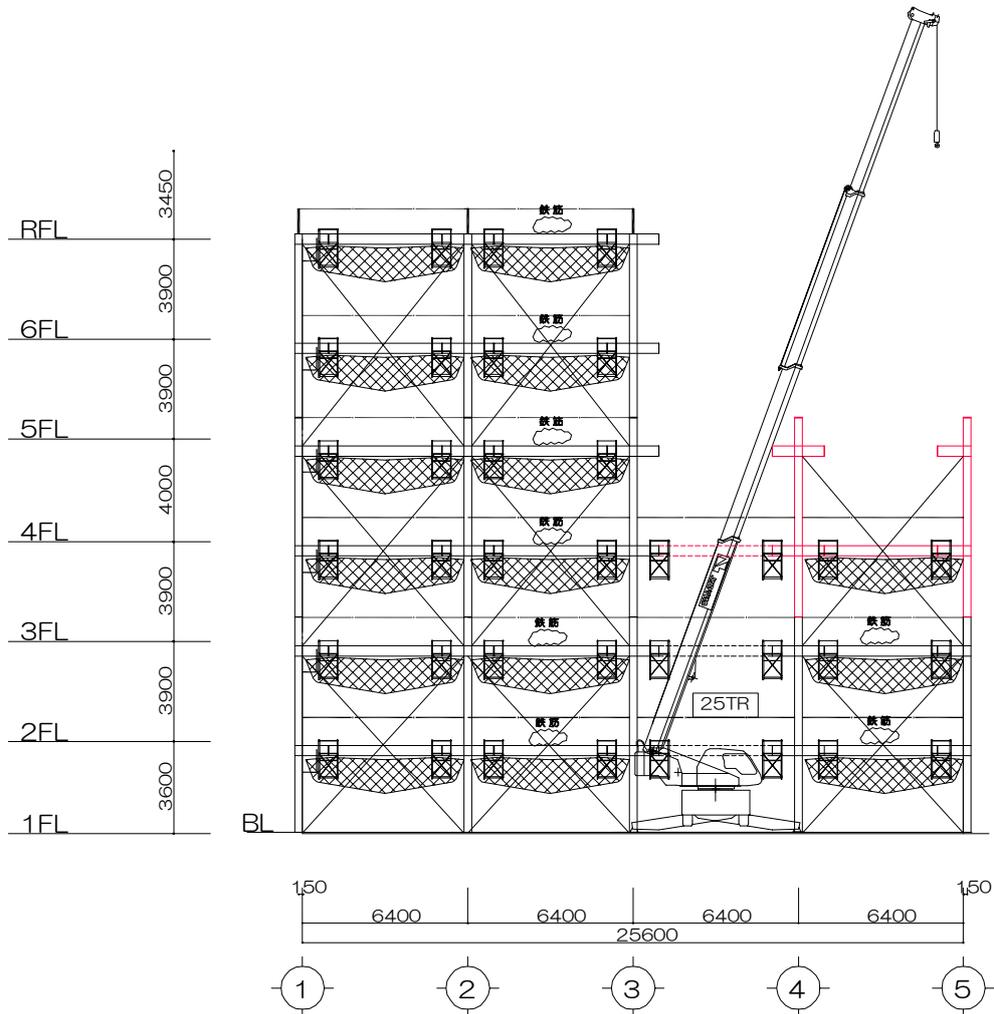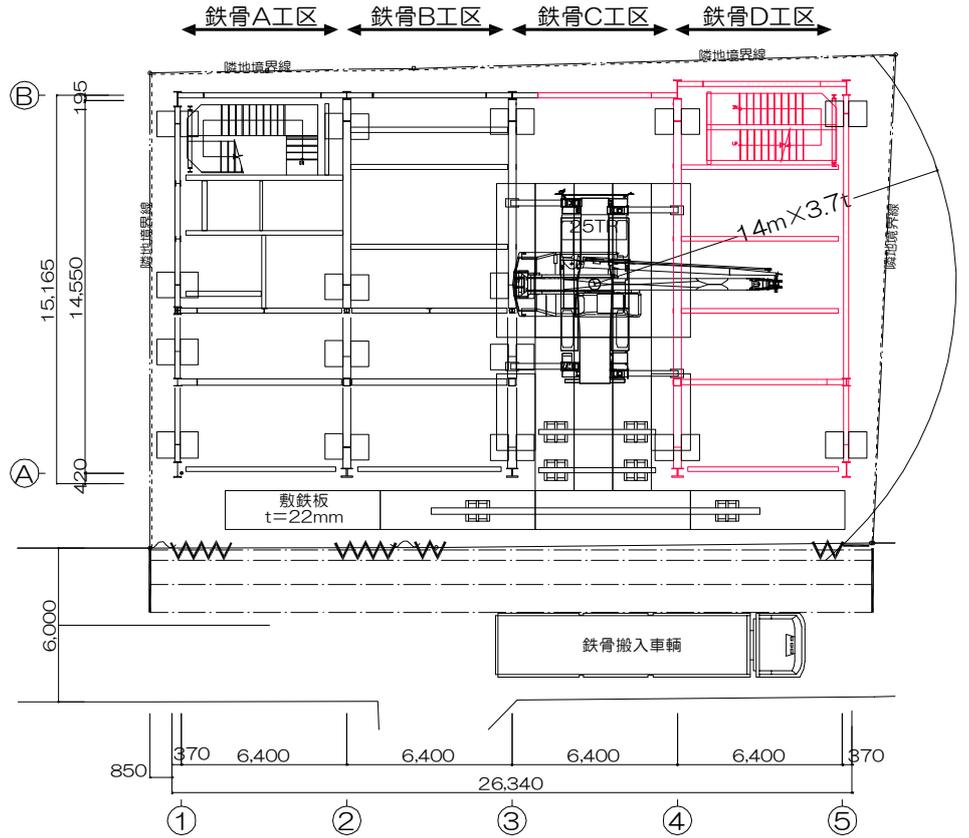

11日目

7/26 (火)



工区	建方部材	数量
D	4F足場	3
	5G	5
	5B	5
	5FD	2
	5F足場	3
	v	2
	5F鉄筋	13
	5FHTB	1
	計	34
荷受	c	2

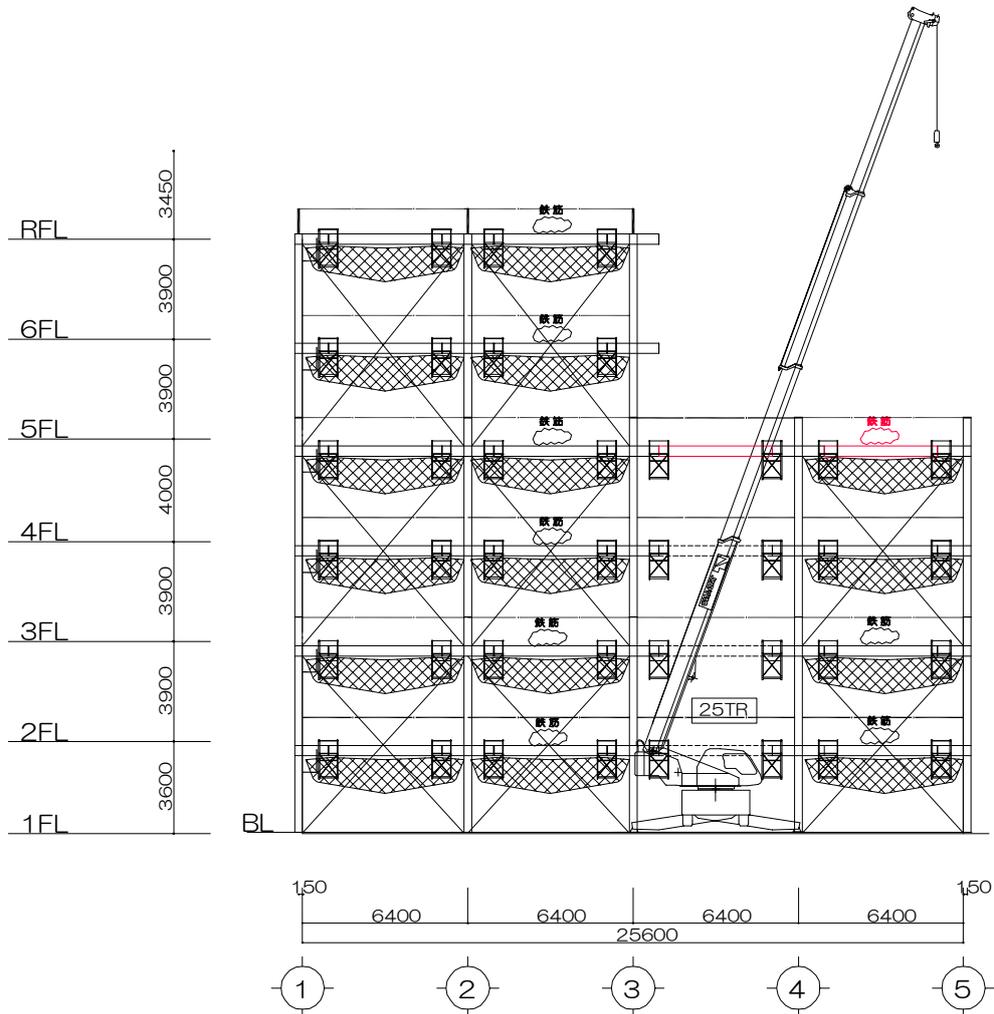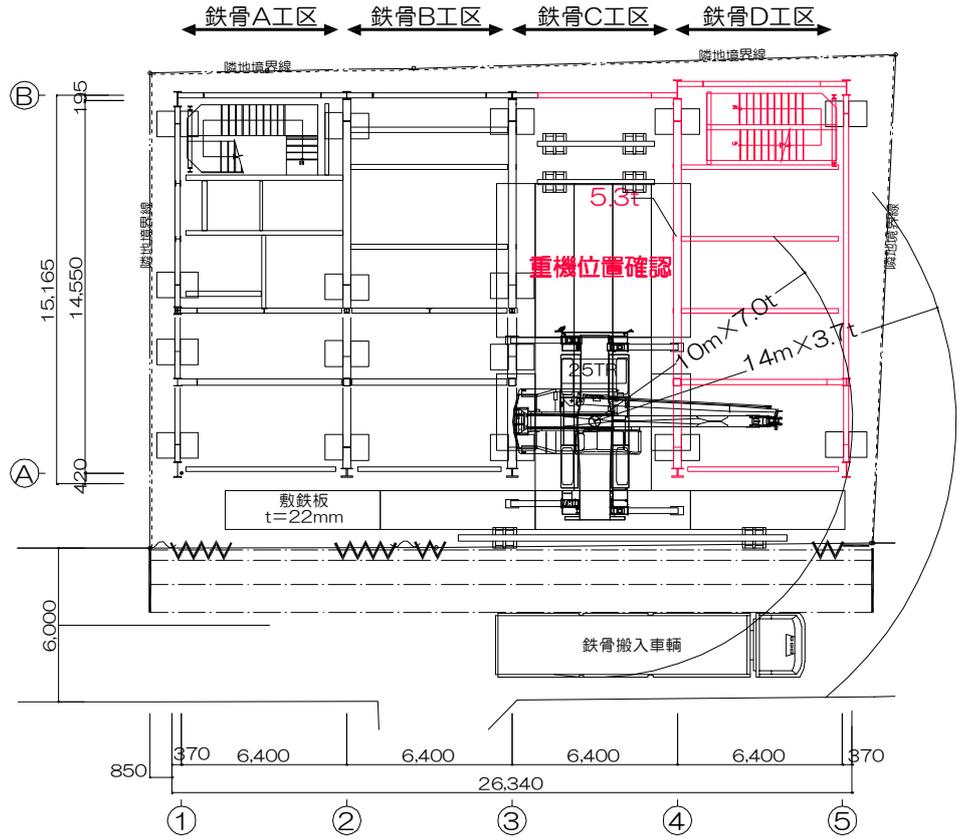

12日目

7/27 (水)



工区	建方部材	数量
D	c	2
	階段間柱	1
	鉄骨階段	4
	3C	2
	6G	6
	6B	3
	6FD	3
	6F鉄筋	5
	6FHTB	1
	鉄骨階段	2
	計	29
荷受		
	c	2

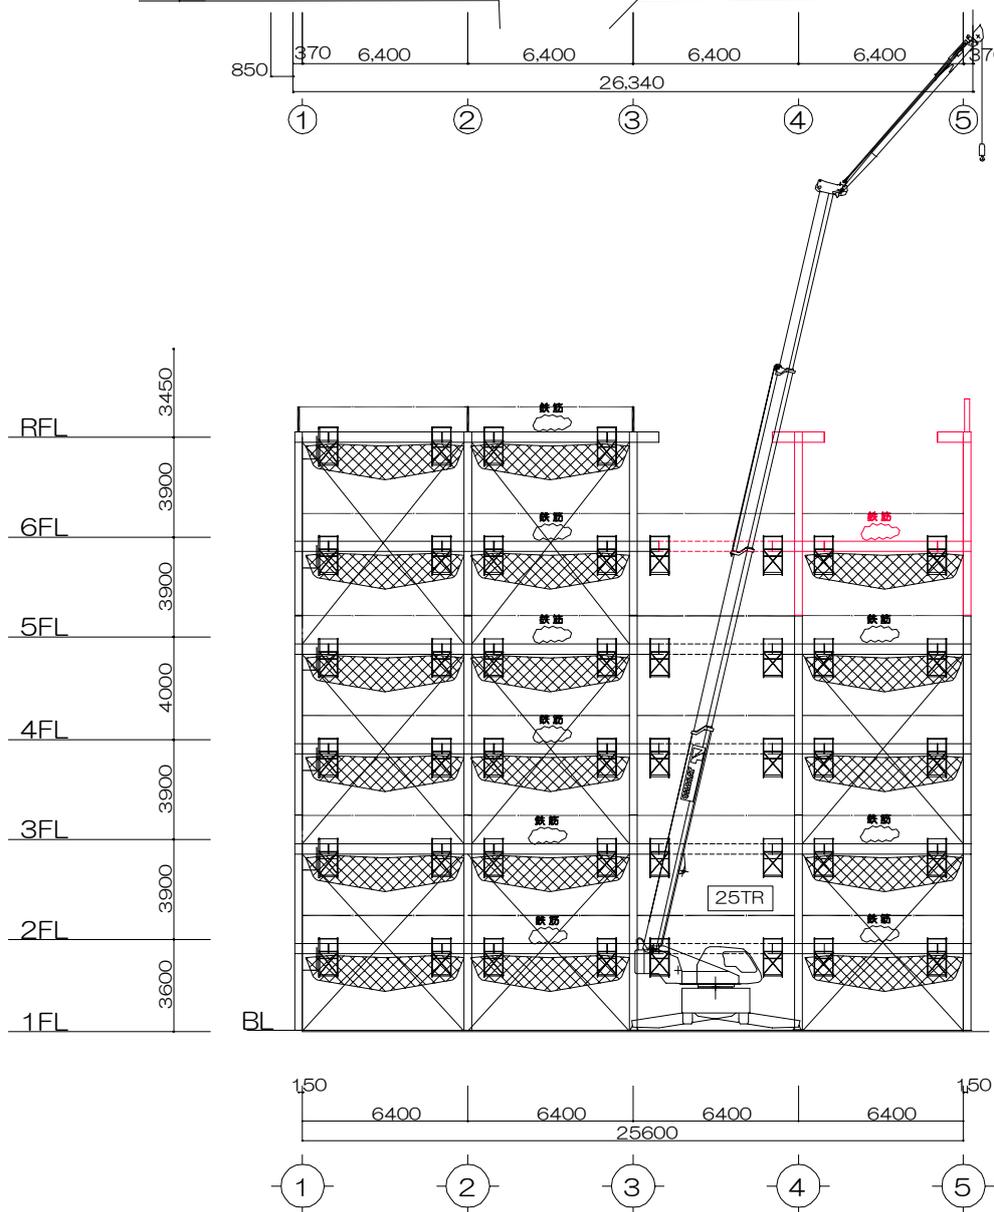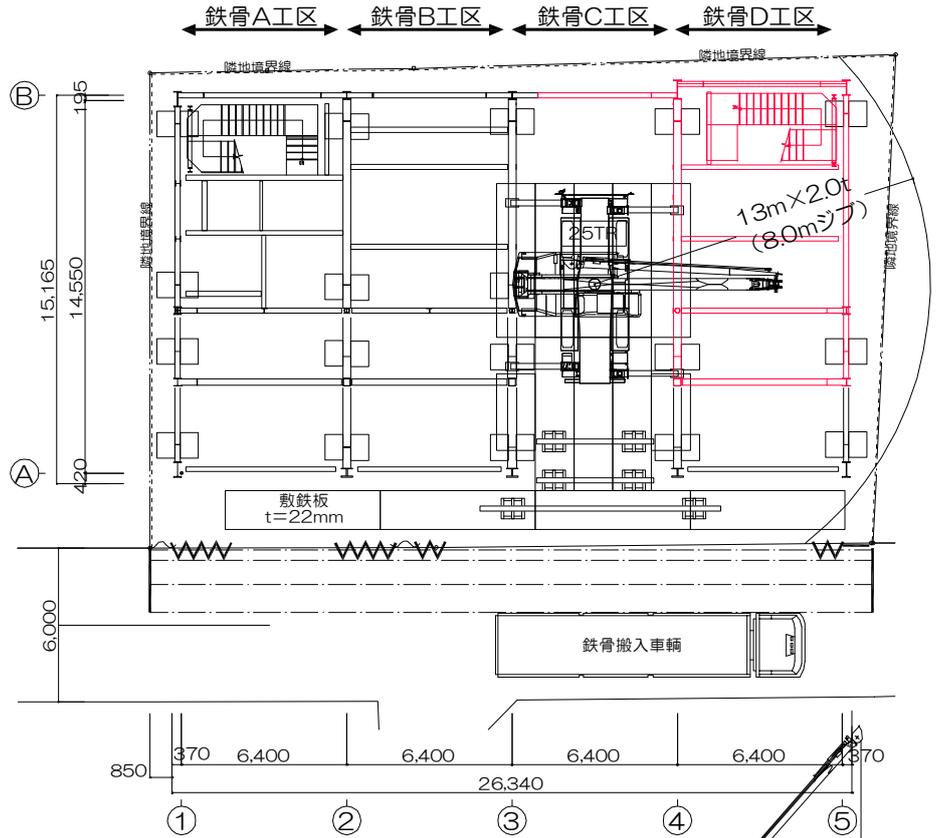

13日目

7/28 (木)

工区	建方部材	数量
D	c	2
	RG	5
	RB	3
	RFD	3
	RFHTB	1
	目隠柱	10
	目隠梁	16
	計	40
荷受	設備柱	2
	設備梁	17

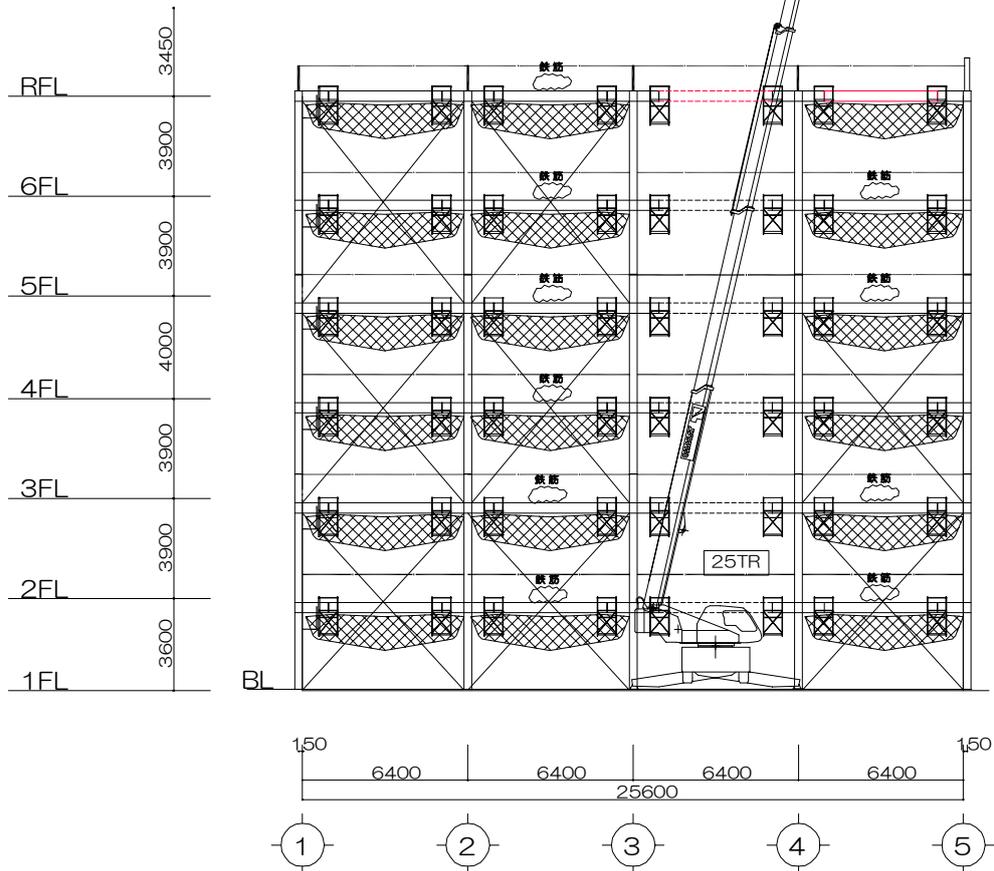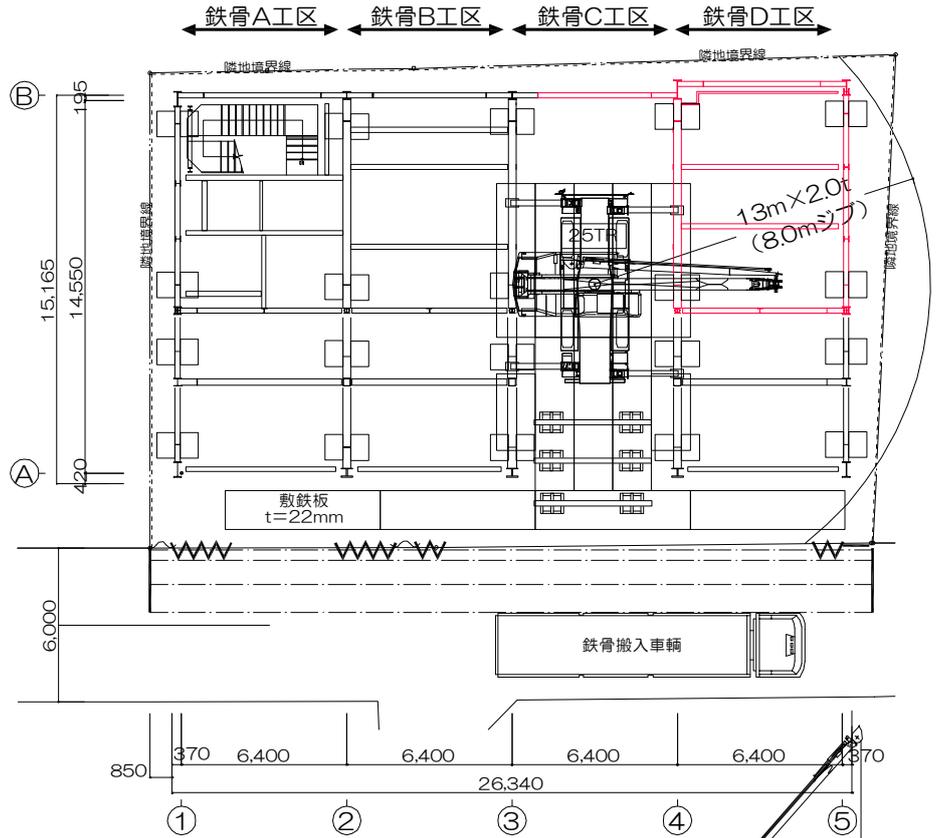

14日目

7/29 (金)

工区	建方部材	数量
D	設備柱	2
	設備梁	17
	計	19

10:00 25TR移動





鉄板引揚げ



13:00 建方再開

工区	建方部材	数量
D	2B	4
	3B	4
	3FD	2
	4B	4
	計	14

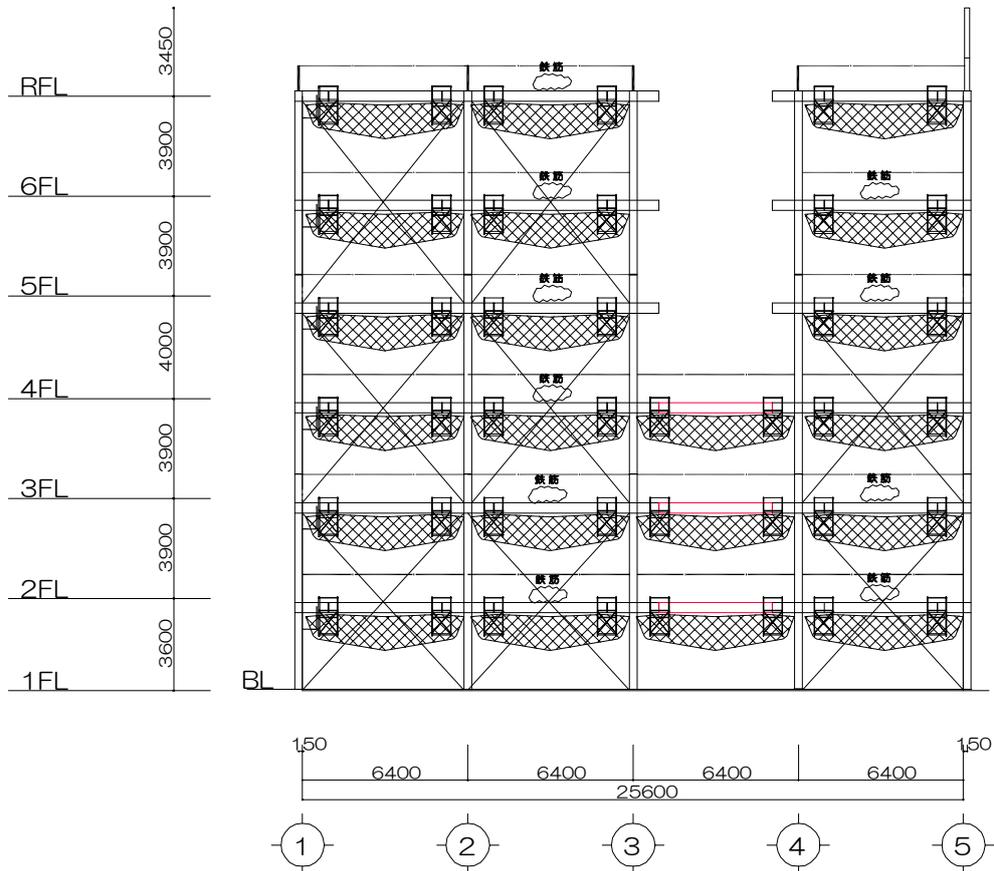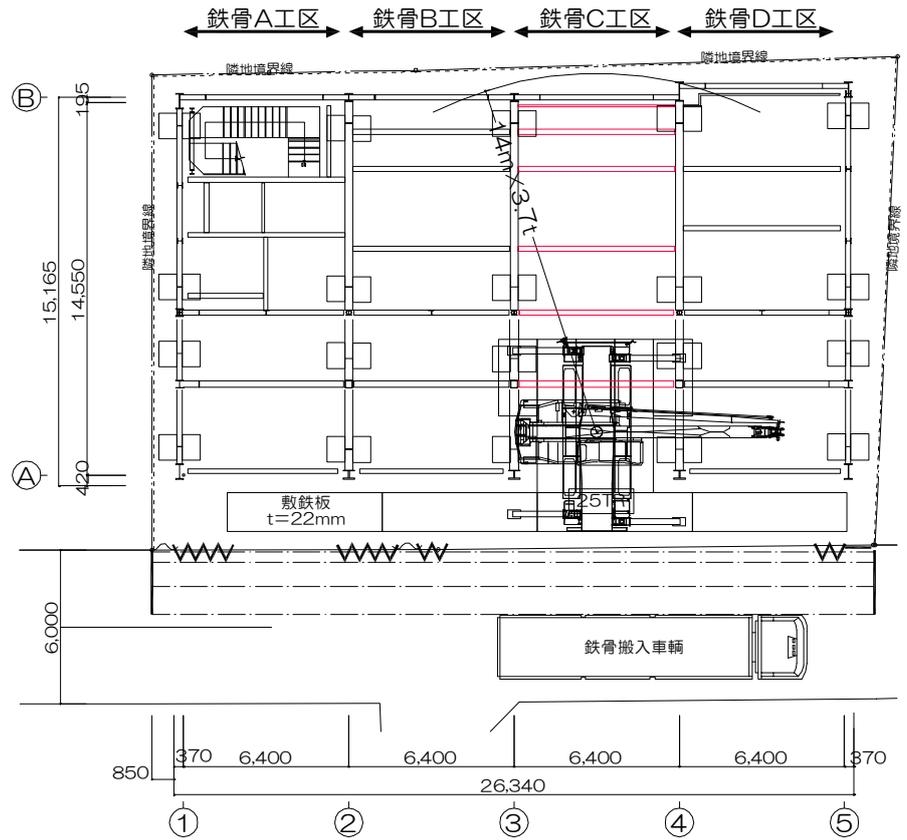

15日目



7/30 (土) 9:00開始

工区	建方部材	数量
D	4F鉄筋	10
	5B	4
	5FD	2
	6B	5
	RG	1
	RB	4
	目隠柱	2
	目隠梁	8
	設備梁	5
	計	41

25TR引揚げ



鉄板引揚げ

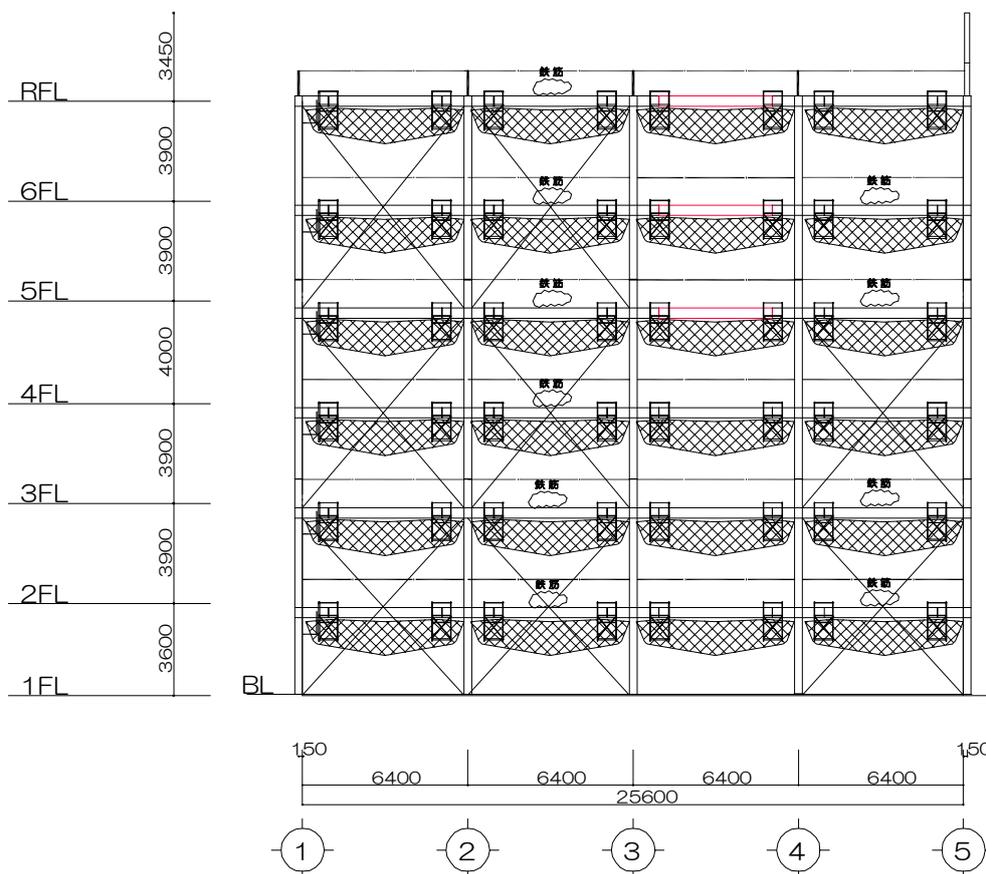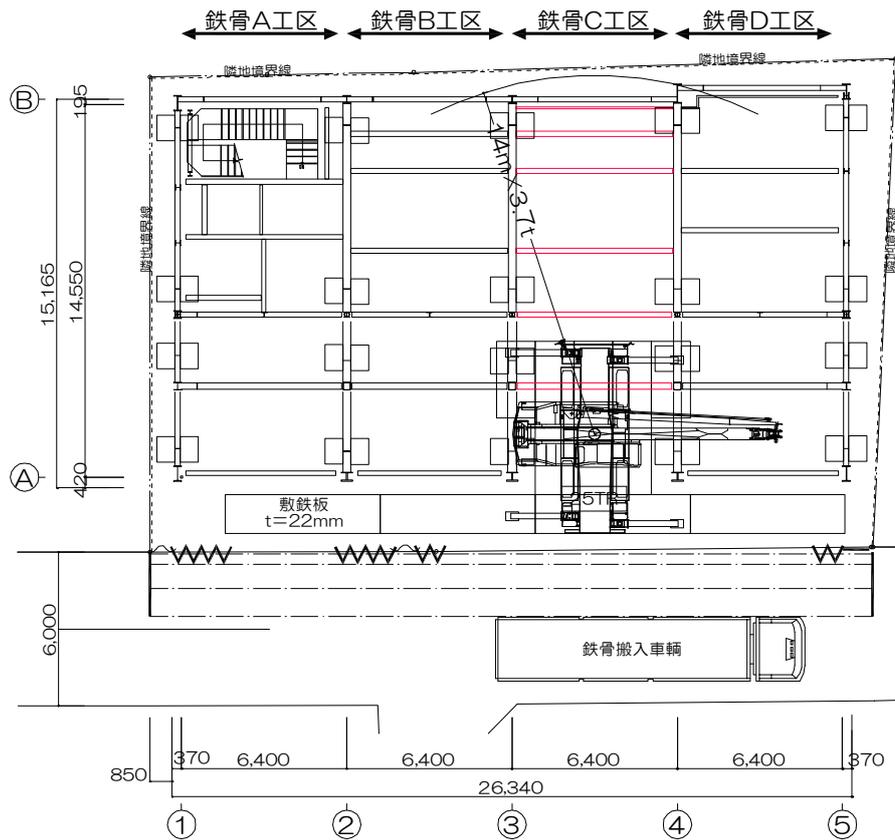

16日目

